

Change Order to the Construction Contract for the Taxiway H Phase 1 Reconstruction Project

Item 9


June 20, 2024

Thomas Bartlett, Deputy Director, Aviation



Background

Scope: Reconstructs a section of Taxiway H with drainage and airfield improvements and relocates a Federal Aviation Administration duct bank and communications fibers.

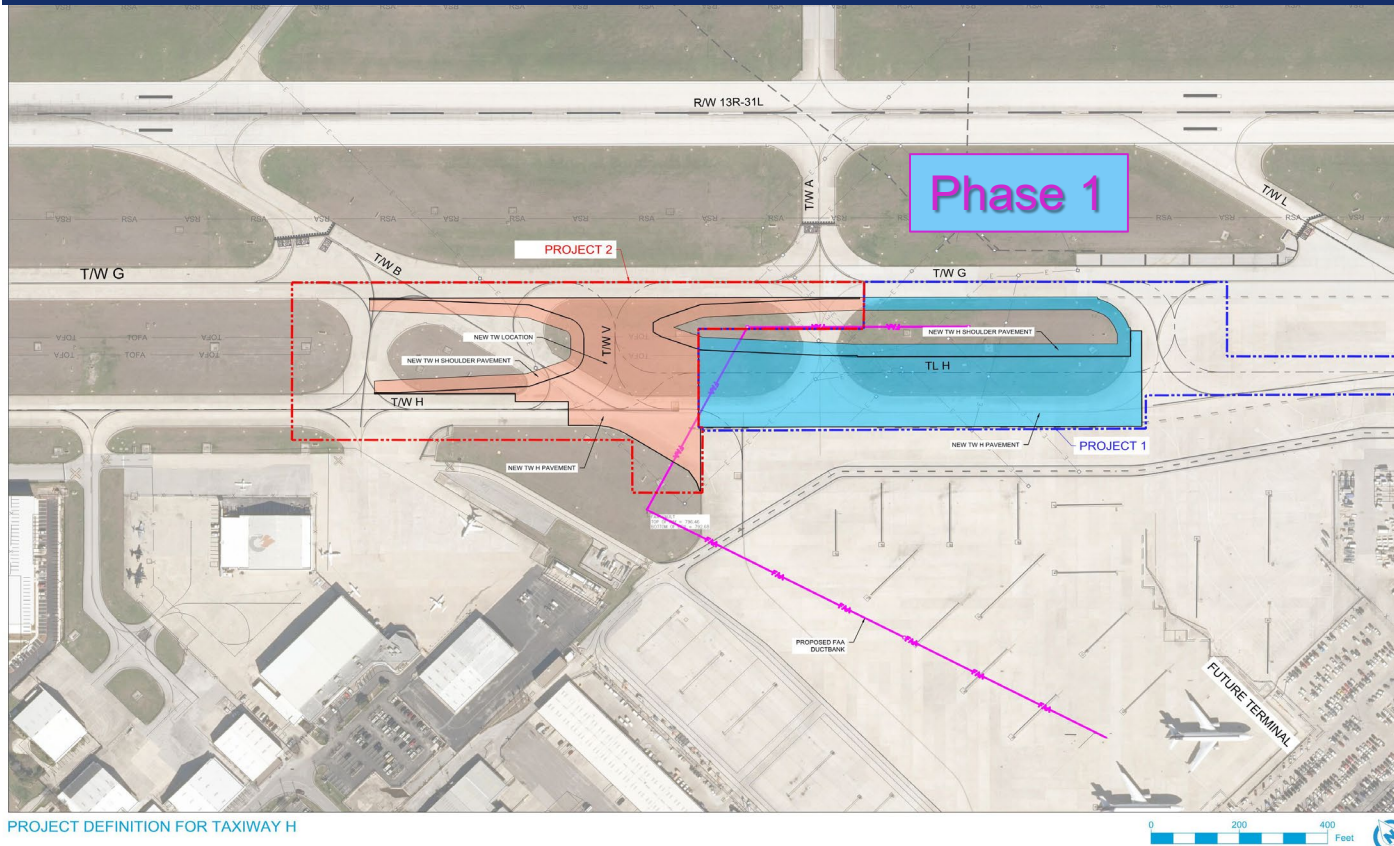

Original Contract Value

- \$12,705,802.30

Previously Approved Change Orders

- \$97,304.70


Current Value:

- \$12,803,107

Funding Sources:

- Federal Aviation Administration Grant & Airport Interim Financing

Change Order

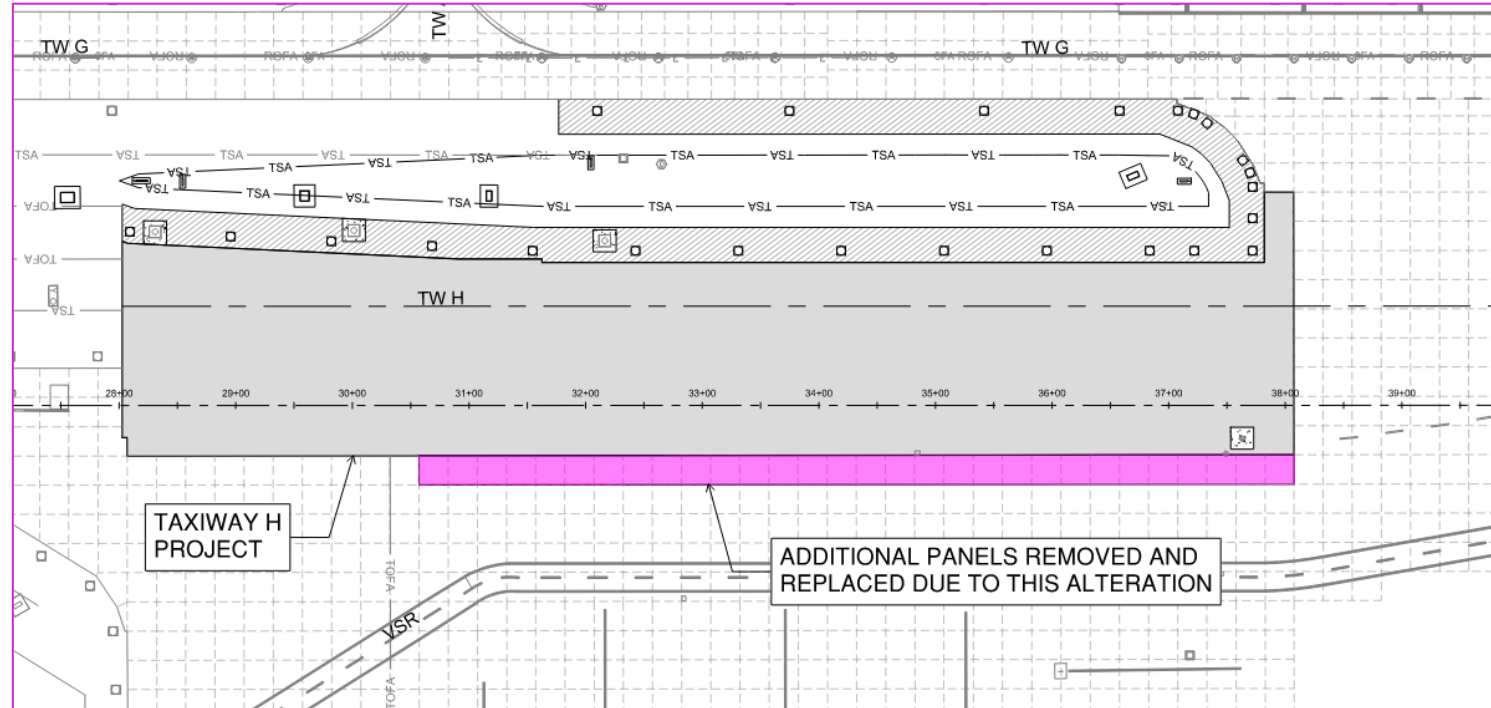

- Change order approves the modification of pavement elevation to remove 1 row of 30 concrete panels & construct a temporary sloped asphalt tie-in to existing pavement to accommodate construction of new terminal.
- As the new terminal project progresses, the temporary pavement area will be demolished, and proposed terminal pavement will tie-in to the TW H project pavement at the required elevation.

Change Order



- Approves the Change Order amount in the amount of \$373,871.02 and increases the contract by 7 days.
 - New contract amount: \$13,176,978.02
- Action will also reallocate \$495,000 from Airfield Package 6-7 project into the Taxiway H Phase 1 Project for the change order and an additional \$121,128.98 for owner's contingency funds.

Change Order to the Construction Contract for the Taxiway H Phase 1 Reconstruction Project

Item 9

June 20, 2024

Thomas Bartlett, Deputy Director, Aviation

